

# Public Safety Building



MONTHLY REPORT 12 March 2022 PREPARED BY NOVA PARTNERS, INC.



### **Project Information**

City of Palo Alto Public Safety Building

Architect
RossDrulisCusenbery

General Contractor
Swinerton Builders

Construction Manager Nova Partners The Public Safety Building (PSB) is a new three-story police station, fire administration, and emergency communications and operations facility. The PSB will be located on an existing City-owned parking lot at 250 Sherman Ave. The new PSB includes two full-block subterranean floors of secure police and staff parking and makes accommodation for a site utility yard, a public plaza, a 135ft communications tower and exterior site buildings.

The primary goal of this project is to create a state-of-the-art facility that brings the City's public safety departments together in a structure which meets current building codes and standards, including the Essential Services Buildings Seismic Safety Act, while serving the public's needs as a civic focal point.

The new PSB project consists of a ballistically rated exterior, coupled with technology-heavy communications systems and sufficient back-up power to allow the building to function in the event of an emergency. Other features include:

- Public plaza and main entry on Birch Street
- · Multi-purpose training room and meeting space
- Secure operations yard with large public safety vehicle parking
- A water exclusionary shoring system ('cut-off wall") to minimize groundwater pumping during construction
- Connection to PV panels on California Avenue Parking Garage provides clean energy

The construction contract was awarded to Swinerton Builders and work began on March 1<sup>st</sup> 2021. Completion is anticipated for Summer of 2023.



### **Activities**

#### Activities Completed March 2022:


- Ongoing dewatering
- Completed 1st pour of Level 1 concrete slab.
- Completed placement of Basement Level 1 vertical concrete.
- Ongoing MEP rough-in.

#### **Upcoming Activities April 2022:**

- Ongoing dewatering
- Complete placement of Level 1 concrete slab.
- Level 1 vertical element concrete installation.
- Ongoing MEP rough-in.

Completion is anticipated in Summer 2023.

# **Project Photos**






Concrete and rebar in place for Level 1 concrete slab.

# **Project Photos**



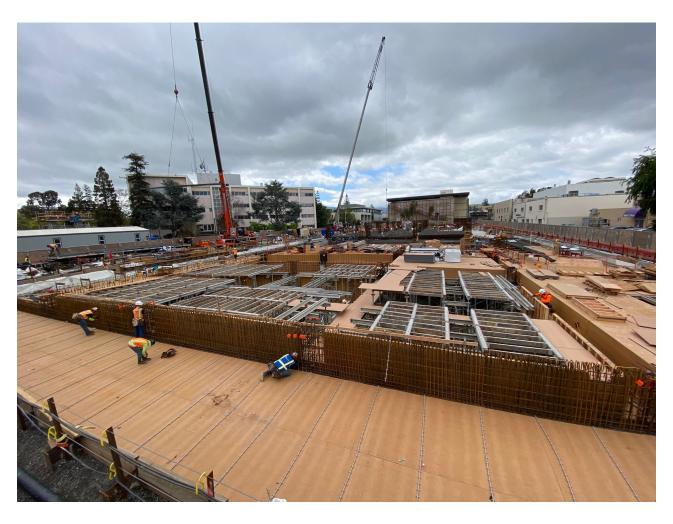

Formwork in place for Level 1 concrete slab.
