# Rinconada Park Restroom Project Update

**Community Meeting** 

February 23, 2023



#### **Meeting Agenda**

- Project Update
- Restroom Update
- Project Schedule
- Questions and Comments



#### Rinconada Park





# Rinconada Park Project Update



# Rinconada Park Long Range Plan Long Range Plan Adopted by council in 2017 Project Goals

- Maintain existing character of the park
- Create better connection and awareness to all the community facilities that exists around and within the park
- Coordination and update of Park resources and amenities to reflect current and future needs of park users and guests
- Respond to park usage as it relates to surrounding uses and neighborhood
- Accessibility and infrastructural improvements
- Coordination of user group objectives



# Rinconada Park Long Range Plan





#### **Project Update**

#### Rinconada Park Long Range Plan Community Meetings

```
Meeting #1: 4/18/12
Meeting #2: 6/5/12
Meeting #3: 8/2/12
Meeting #4: 9/12/13
```

Long Range Plan Adopted: 2017 (delay for JMZ Design)

#### **Phase 1 Community Meetings**

Meeting #1: 2/21/19 Meeting #2: 4/4/19 Meeting #3: 9/24/19

Phase 1: Completed spring of 2022 Phase 1A: Restroom 2023-2024


Phase 2: 2025

#### **Project Web Page**

www.cityofpaloalto.org/parkrestrooms



#### Phase 1 Rinconada Park Renovations

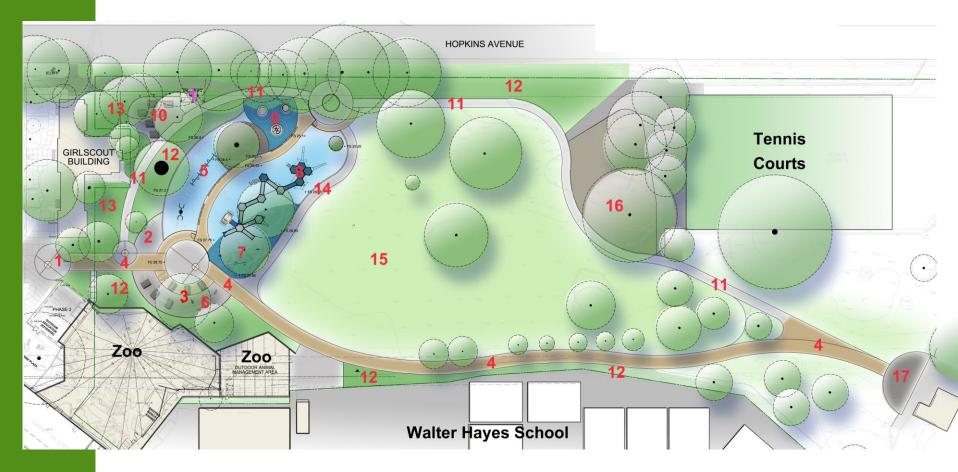



# Rinconada Park Restroom Update



#### **Proposed Restroom Layout**

#### **Restroom Features**

- Two ADA stalls (unisex)
- Easily accessible service area
- Anti graffiti exterior
- Time locks nightly at 10pm
- Easily cleaned interiors
- Restroom to be clean everyday




Restroom Layout





#### **Rinconada Park Restroom Exhibit**

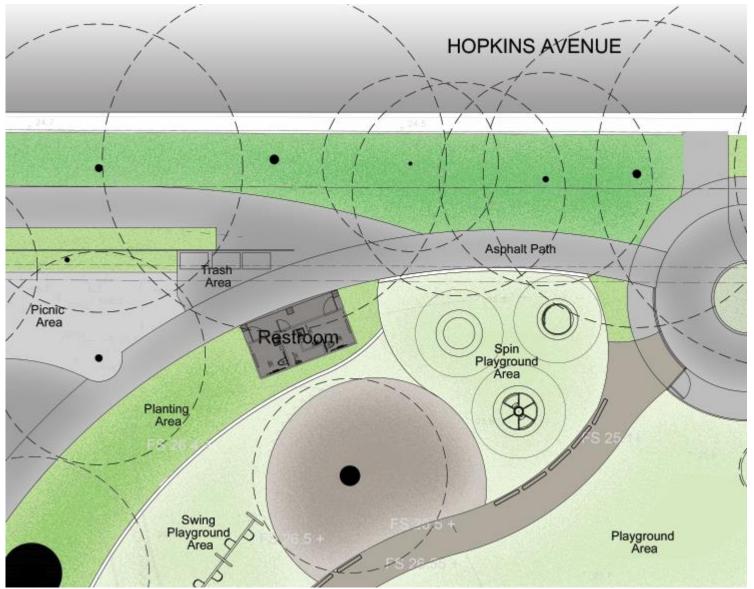



### **Project Schedule**

- City to Purchase Restroom April 2023
- Prefabricated Restroom Construction 10-12 months
- Site construction 2 months at start of 2024



### **Questions & Comments**



#### **Project Status**

www.cityofpaloalto.org/parkrestrooms



# Rinconada Park Restroom Update

